


Look Ahead View for April 12th, 2018

Foundations Continuing

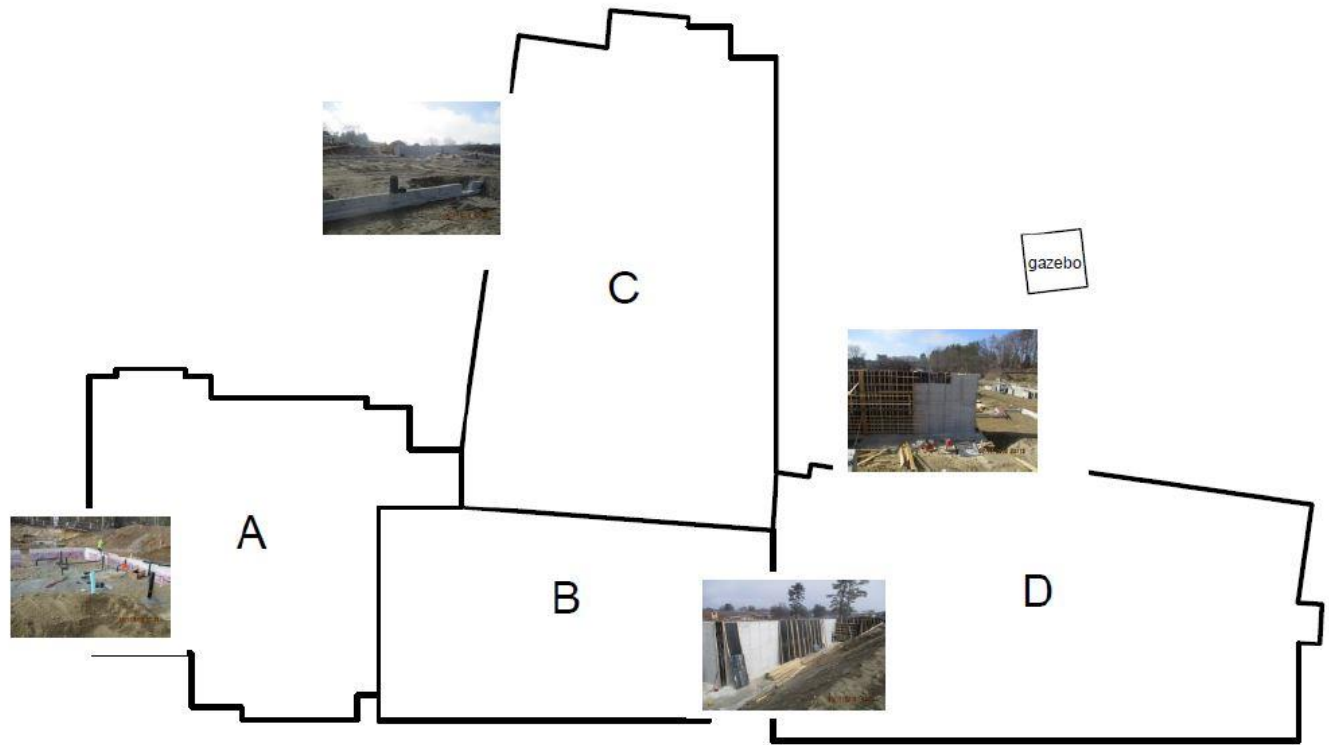

Photos from week of April 9th, 2018

Views of the foundation work are shown on the plan above as thumbnails to indicate where work was done. Progress is significant on the foundations. As sections are cured, they are waterproofed and backfilled. Work on electrical and plumbing within the sections is ongoing. Pictures of work progress follow.

Look Ahead View for April 12th, 2018



The site is very busy with 5 trades on site including Excavating, Concrete, Plumbing, Electrical and Waterproofing. Next week will see the addition of the Steel workers and the onsite totals will go from approximately 42 people to over 60 people a day.

Look for structural steel deliveries starting the week of April 17th. The crane that will move the steel will be delivered and erected on April 18th. Next week, during school vacation, the sewer connection at the east end of the site will be completed.

MSBA

Last week, two members of the MSBA, our State funder, attended the weekly construction meeting. They also toured the site to view the progress. They will continue to attend meetings monthly.

Look Ahead View for April 12th, 2018

More Information

For more information about the New Elementary School project, follow us on:

www.Millis.Org Look on the front page under News and Notices for the current Look Ahead View and under Boards and Committees for the Elementary School Building Committee page to find prior Look Ahead Views.

www.Facebook.com/MillisSchoolProject/ Look for current posts about the project.

www.MillisMedia.org Look under Videos for recordings of the Elementary School Building Committee meetings and other relevant events.

The Elementary School Building Committee
