


## Look Ahead View for May 7th, 2018

### We Are Out of the Ground!

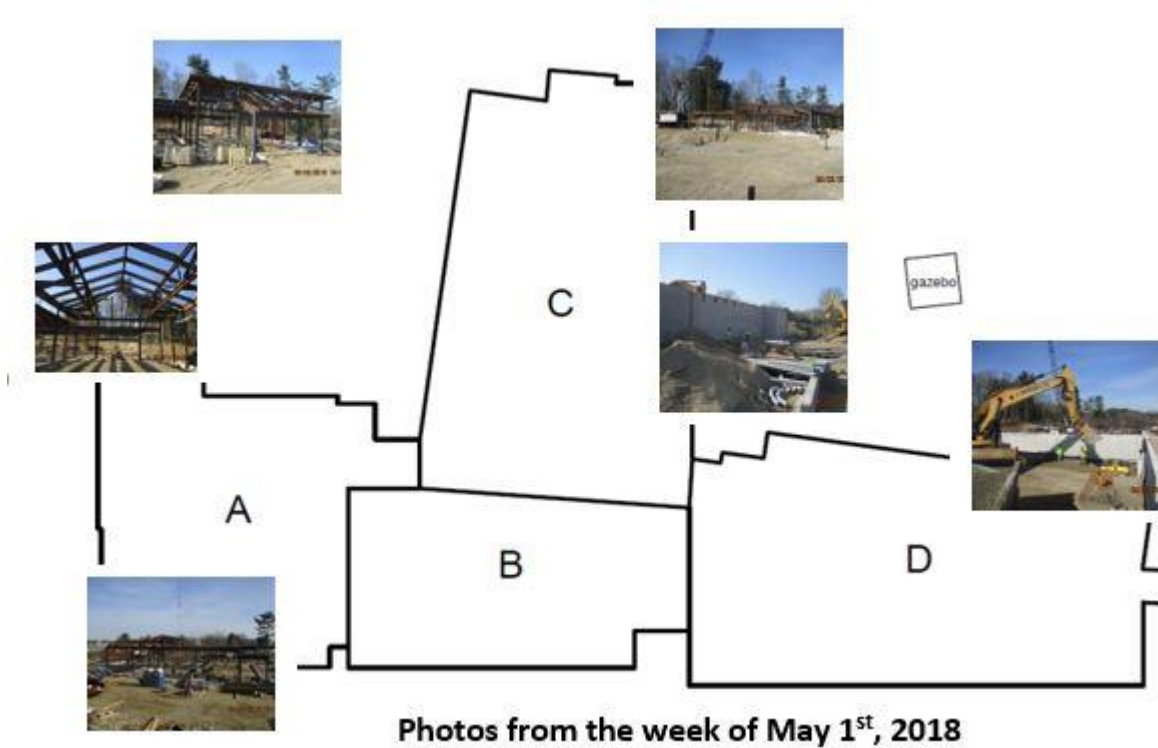

The building is “out of the ground” as they say in the construction industry. Foundation work is mostly complete, with some additional footings for the D wing yet to be placed. That work will be completed in the next few weeks. The completed steel work shown above and below is the structure for the cafetorium and A wing. C wing steel erection is next and has already started. The steel framework will continue through the end of June.

Last week a larger crane was brought to the site and it’s a big one. It will stay onsite until the steel is completed.



# Look Ahead View for May 7th, 2018

Pictures of work progress follow.



## **Look Ahead View for May 7th, 2018**

The site is very busy with 6 trades: Excavating, Concrete, Plumbing, Electrical, Waterproofing and Steel Erectors. We continue to be on schedule and on budget.

### **MSBA**

Last week, two members of the MSBA, our State funder, attended the weekly construction meeting. They also toured the site to view the progress. The first payment from the MSBA was received on May 4 for \$2,689,611.00. This reimbursement covers the MSBA's portion of the construction costs incurred to date. From here on, reimbursements will be transferred on monthly schedule.

### **More Information**

For more information about the New Elementary School project, follow us on:

[www.Millis.Org](http://www.Millis.Org) Look on the front page under News and Notices for the current Look Ahead View and under Boards and Committees for the Elementary School Building Committee page to find prior Look Ahead Views.

[www.Facebook.com/MillisSchoolProject/](http://www.Facebook.com/MillisSchoolProject/) Look for current posts about the project.

[www.MillisMedia.org](http://www.MillisMedia.org) Look under Videos for recordings of the Elementary School Building Committee meetings and other relevant events.

### **The Elementary School Building Committee**
