



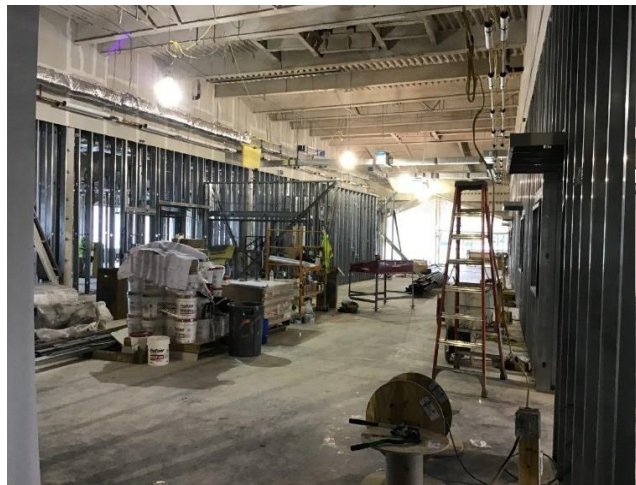

# Look Ahead View for September 23rd, 2018

## School Building Progress

Progress on the site is steady and we are still working toward being able to close the building up by November so that winter work can be done. Watch for exterior masonry work with the new colored exterior walls beginning to be visible. That work will be ongoing.

Interior work continues with electrical, plumbing, HVAC, fire protection, waterproofing and utilities. Drywall will start next week. On average, there are over 65 people a day working on site. The progress being made has kept us on schedule and we are still on budget.

Pictures of work progress follow.

Exterior Looking at South Side of Site	Interior Looking at D Wing
	
Interior Second Floor C Wing Commons/Media Space	Interior Second Floor C Wing Commons/Media Space
	

Look Ahead View for September 23rd, 2018

Exterior Looking at East Wall of C Wing	Exterior Looking at Main Entrance
	
Exterior Looking at Cafeteria Entrance	Exterior Looking at South Side of Site
	



## **Look Ahead View for September 23rd, 2018**

### **More Information**

For more information about the New Elementary School project, follow us on:

[www.Millis.Org](http://www.Millis.Org) Look on the front page under News and Notices for the current Look Ahead View and under Boards and Committees for the Elementary School Building Committee page to find prior Look Ahead Views.

[www.Facebook.com/MillisSchoolProject/](https://www.Facebook.com/MillisSchoolProject/) Look for current posts about the project.

[www.MillisMedia.org](http://www.MillisMedia.org) Look under Videos for recordings of the Elementary School Building Committee meetings and other relevant events.

### **The Elementary School Building Committee**
