

FY22 Paving bid #1:**Chapter 90 Funds**

Available as of July 01, 2021 \$517,367.73

Contractor: Miozzi Inc. \$342,150.95
Police Details: open \$10,179.45
Line Painting: open

Job #1**Farm Street from Acorn Street to Brandywne Terrase: 4,800 feet Completed**

Milling 1.5" of roadway replace with 1.5" of top bituminous concrete.

Job #2**Main Street #1 from Plain Street to Park Road 550 feet Main Street #2 from Exchange Street to Park Road 245 feet**

Milling 1.5" of roadway replace with 1.5" of top bituminous concrete. Completed

Job #3**Ridge Street from Union Street to Auburn Road: 3,600 feet**

Milling 1.5" of roadway replace with 1.5" of top bituminous concrete. Completed

Job #4**DPW Parking lot:**

Fine grading and compacting	\$12,480.00
Superpave Intermediate	\$65,250.00
Funding: DPW project	Total : \$77,730.00 open

FY22 Paving bid #2:**Article 17 - FY22 Spring Town Meeting \$143,805.23**

Contractor:	Lorusso Corporation	Bid amount:	\$109,712.00
Police Details:		Bid amount:	\$4,320.00
10% Contingencies:		Bid amount:	\$11,403.20
		Total:	\$125,435.20

Job #1**Spring Street from Main Street to Plain Street: 3,550 feet**

Milling 1.5" of roadway replace with 1.5" of top bituminous concrete.



Spring Street Paving

Millis, MA




September 7, 2021

1 inch = 558 Feet



www.cai-tech.com

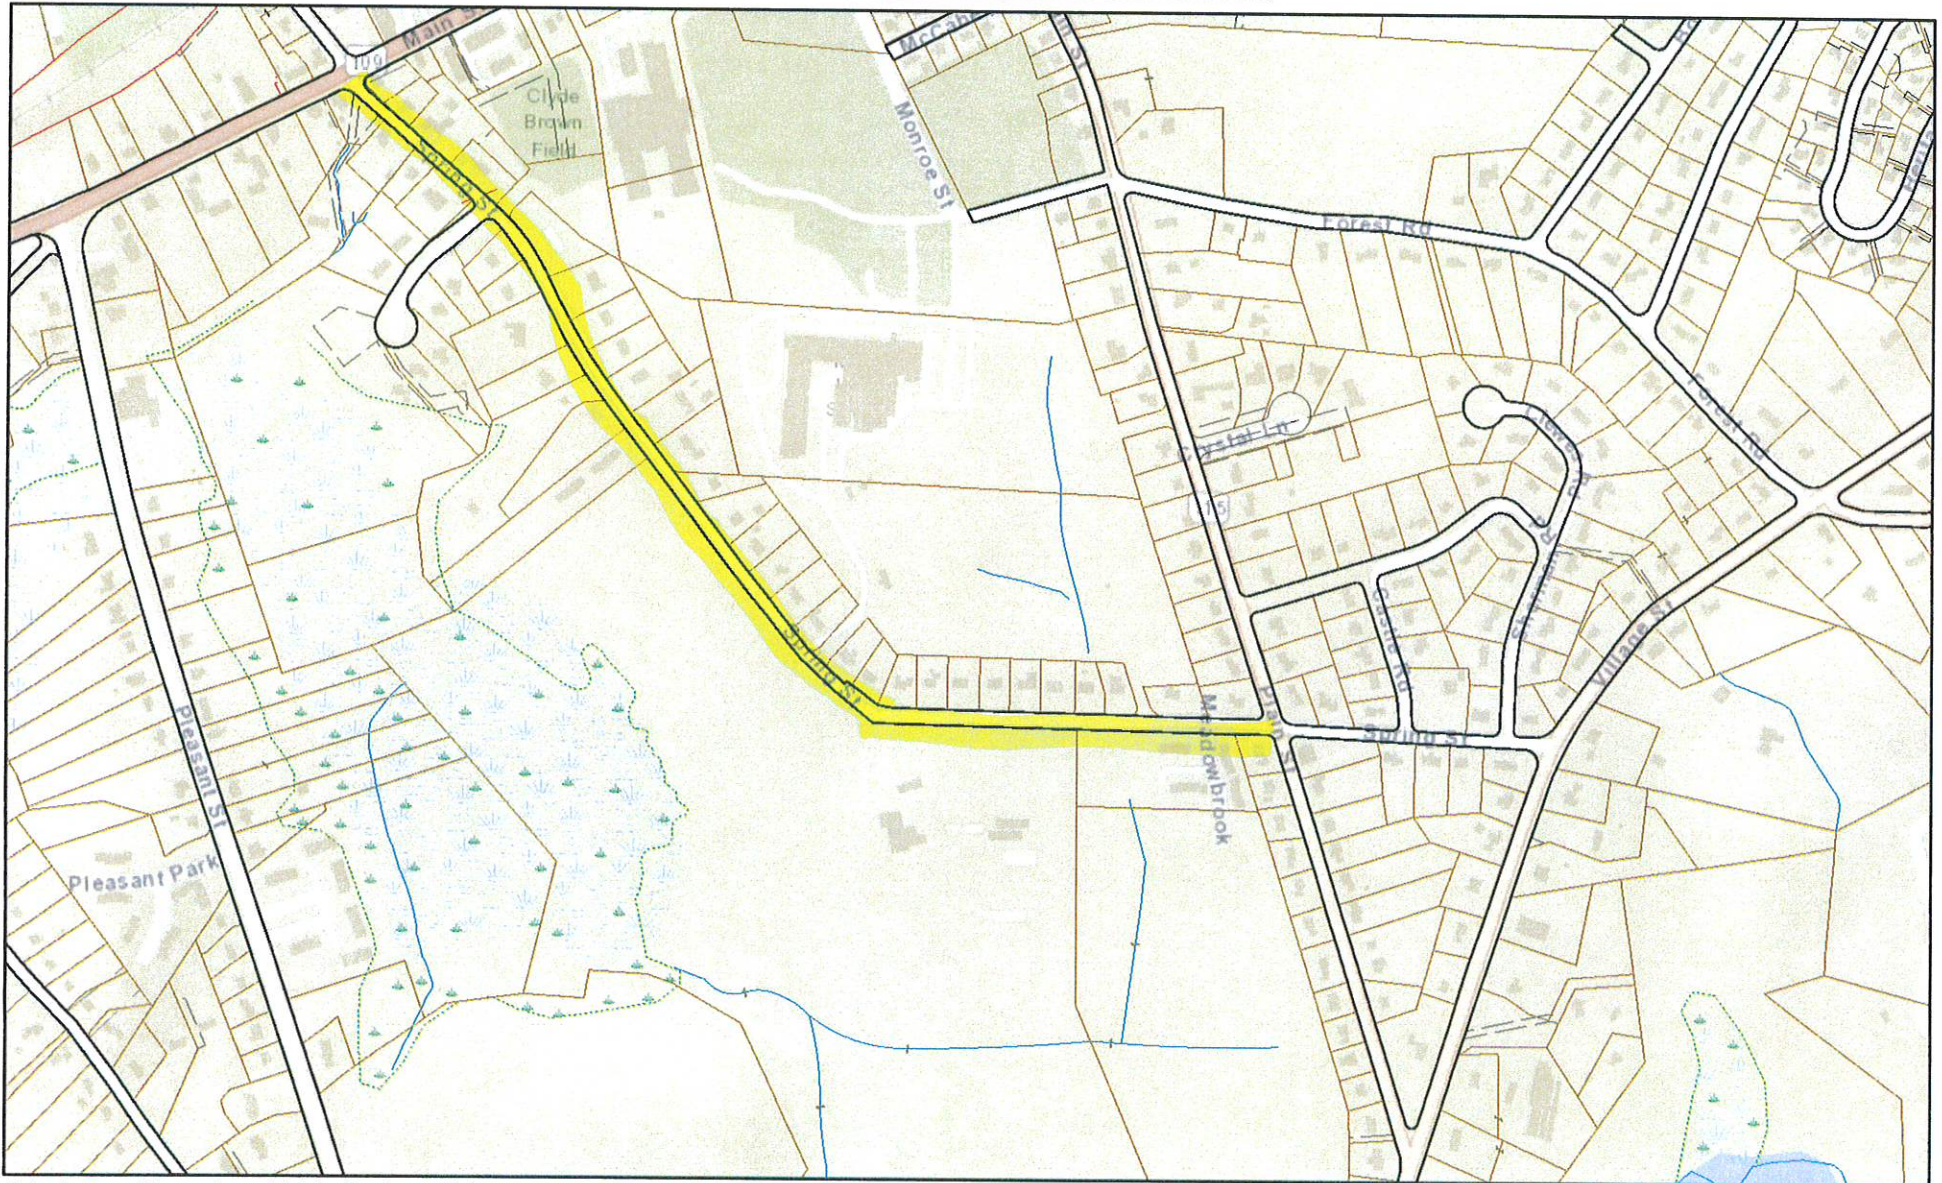

Data shown on this map is provided for planning and informational purposes only. The municipality and CAI Technologies are not responsible for any use for other purposes or misuse or misrepresentation of this map.

Item 1.) (Base Bid) - Spring Street (from Main Street to Plain Street). 1-1/2" Mill and Pave					9/3/2021
					Prepared By: GCG Associates, Inc.
FY22, Annual Street Paving Project Town of Millis					Item 1 (BASE BID)
Contract 2					3,550' +/- L.F. x 21' +/- W
Lorusso - Low Bid					Mill, 1-1/2" Top
Contract Award Item 1 (BASE BID)					Level/Patch-monoberm
					Spring
Item#	Description	Unit	Base Unit Price	Qty	Total Amount
120.1	Unclassified Excavation	C.Y.	\$ 1.00	20	\$ 20.00
151.1	Gravel Borrow - Type C	C.Y.	\$ 1.00	20	\$ 20.00
			\$ -	0	\$ -
220	Drainage Structure (Adjusted)	Ea.	\$ 250.00	26	\$ 6,500.00
220.2	Drainage Structure (Rebuilt)	V.F.	\$ 290.00	5	\$ 1,450.00
222.3	Frame and Grate (or Cover) - Municipal Standard	Ea.	\$ 425.00	6	\$ 2,550.00
223.2	Frame and Grate (or Cover) Removed and Discard	Ea.	\$ 1.00	6	\$ 6.00
357.06	6" Gate Box	Ea.	\$ 100.00	8	\$ 800.00
358	Gate Box Adjusted	Ea.	\$ 200.00	2	\$ 400.00
415.1	Pavement Standard Milling	S.Y.	\$ 2.75	8280	\$ 22,770.00
451	HMA for Patching	Ton	\$ 1.00	10	\$ 10.00
452	Asphalt Emulsion for Tack Coat. (0.08 Gal. per S.Y.)	Gal.	\$ 5.00	662	\$ 3,310.00
453	HMA Joint Sealant	FT.	\$ -	0	\$ -
460.22	HMA - Superpave Surface Course - 9.5 (SSC - 9.5)(1.5") include Monolithic Berm	Ton	\$ 85.00	750	\$ 63,750.00
			\$ -	0	\$ -
460.52	HMA - Superpave Leveling Course - 9.5 (SSC - 9.5)	Ton	\$ 80.00	25	\$ 2,000.00
472	Temporary HMA for Patching	Ton	\$ 1.00	10	\$ 10.00
697.1	Silt Sack	Ea.	\$ 100.00	6	\$ 600.00
702	Hot Mix Asphalt (HMA) DRIVEWAY	Ton	\$ 81.00	40	\$ 3,240.00
751	Loam Borrow	C.Y.	\$ 85.00	25	\$ 2,125.00
765	Seeding	S.Y.	\$ 1.00	150	\$ 150.00
999.002	Temp Traffic Control	L.S.	\$ 1.00	1	\$ 1.00
Base Bid Construction					\$ 109,712.00
999.001	Police Details** Town pays details directly and are not included in bid	Hour	\$ 60.00	72	\$ 4,320.00
Base Bid Construction and Police					\$ 114,032.00
10% Contingencies					\$ 11,403.20
Total Construction					\$ 125,435.20
*DPW retain \$3000 for Xwalks/Stop Bars					
